

ID	Task Name	Duration	Start	Finish	October			November			December			January			February			March					
					E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E		
1	20 Colonial Drive, Newport Beach, CA	121 days	Mon 10/4/21	Wed 3/30/22																					
2	Notice to Proceed	2 days	Mon 10/4/21	Tue 10/5/21																					
3	Notice to Proceed	0 days	Mon 10/4/21	Mon 10/4/21																					
4	Mobilization	2 days	Mon 10/4/21	Tue 10/5/21																					
5	Demolition	26 days	Mon 10/4/21	Mon 11/8/21																					
6	Removal of Existing 6" Cans Lights at Lower Level	2 days	Mon 10/4/21	Tue 10/5/21																					
7	Demolition in Kitchen & Casita Bathroom	5 days	Mon 10/4/21	Fri 10/8/21																					
8	Meeting Onsite with Artisan Landscape and Right Quarters	1 day	Tue 10/5/21	Tue 10/5/21																					
9	Confirm all RO Numbers for Doors and Windows.	1 day	Wed 10/6/21	Wed 10/6/21																					
10	Electrical Demolition at Upper Level	2 days	Mon 10/11/21	Tue 10/12/21																					
11	Demolition of Bathroom Fixtures	5 days	Mon 10/11/21	Fri 10/15/21																					
12	Soffit Removal in Kitchen and Laundry Room	5 days	Mon 10/11/21	Fri 10/15/21																					
13	Safe off All Plumbing in Bathrooms	1 day	Tue 10/12/21	Tue 10/12/21																					
14	Remove refrigerator and freezer into garage	1 day	Wed 10/13/21	Wed 10/13/21																					
15	Swap out 40 yard container	1 day	Fri 10/15/21	Fri 10/15/21																					
16	Remove closet at living room	1 day	Mon 10/25/21	Mon 10/25/21																					
17	Demolition of Garage Wall & doors for New Header	1 day	Mon 11/1/21	Mon 11/1/21																					
18	Landscape Demolition	5 days	Tue 11/2/21	Mon 11/8/21																					
19	Finishes	97 days	Wed 10/6/21	Mon 2/28/22																					
20	Electrical Rough Ins & Installation of new LED 4" Cans at lower Level	3 days	Wed 10/6/21	Fri 10/8/21																					
21	Electrical Rough Ins & Installation of 4" LED Cans at Upper Level	3 days	Wed 10/13/21	Fri 10/15/21																					
22	Framing in Pot Shelves & Niches	5 days	Mon 10/18/21	Fri 10/22/21																					
23	Entry/ Master/ Top Landing/ Radius Windows at Top Landing	5 days	Mon 10/18/21	Fri 10/22/21																					
24	Repair all Framing from Soffit Removal In Kitchen & In Laundry Room	3 days	Wed 10/20/21	Fri 10/22/21																					
25	New Frame Wall In Living Room to Accept New Built Ins	5 days	Mon 10/25/21	Fri 10/29/21																					
26	Installation of Shower Blocks at Mater Shower/ Shower Bench & Soap Niche	1 day	Mon 10/25/21	Mon 10/25/21																					
27	Installation of Shower Blocks at Secondary Shower	1 day	Mon 10/25/21	Mon 10/25/21																					
28	Rough Ins in Bathrooms for new Fixtures	2 days	Tue 10/26/21	Wed 10/27/21																					
29	Plumb Showers Drains/ Fixtures	2 days	Thu 10/28/21	Fri 10/29/21																					
30	Placement of New Header & Framing Members for Garage Opening	3 days	Tue 11/2/21	Thu 11/4/21																					
31	Installation of New Overhead Door & Trims for Garage	2 days	Fri 11/5/21	Mon 11/8/21																					
32	Installation of New Hot Mop Shower	1 day	Tue 11/9/21	Tue 11/9/21																					
33	Formwork, Reinforcement & pouring of Footings for Casita	7 days	Fri 11/5/21	Tue 11/16/21																					
34	Framing for Casita House	5 days	Wed 11/17/21	Tue 11/23/21																					
35	Insulation in Walls	3 days	Mon 11/22/21	Wed 11/24/21																					


Project: 20 Colonial Drive, New
Date: Fri 10/29/21

Task Milestone Split Summary

Project Summary External Tasks External Milestone Deadline

Progress

ID	Task Name	Duration	Start	Finish	r	October				November			December			January			February			March		
						E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E
36	Dry Wall Finish & Patch Work	3 days	Mon 11/29/21	Wed 12/1/21																				
37	Ceiling Framing, Insulation & Gypsum Board	7 days	Thu 12/2/21	Fri 12/10/21																				
38	New Roofing for Casita	6 days	Mon 12/13/21	Mon 12/20/21																				
39	Installation of Roof Coatings & Rain Gutters	2 days	Tue 12/21/21	Wed 12/22/21																				
40	Interior Paint Walls & Ceiling, Corner Beads & Smooth Coat	9 days	Thu 12/23/21	Thu 1/6/22																				
41	Installation of New Doors & Windows of New Product in Openings	4 days	Fri 1/7/22	Wed 1/12/22																				
42	Paint Doors & Trims	2 days	Thu 1/13/22	Fri 1/14/22																				
43	Rest Room Wall Tiles	3 days	Tue 1/18/22	Thu 1/20/22																				
44	Cabinets in Bathrooms, Closet & Kitchen	5 days	Fri 1/21/22	Thu 1/27/22																				
45	Countertops Installation	2 days	Thu 1/27/22	Fri 1/28/22																				
46	Finish Hardware	3 days	Fri 1/28/22	Tue 2/1/22																				
47	Flooring	6 days	Mon 1/31/22	Mon 2/7/22																				
48	Finish MEP	6 days	Tue 2/8/22	Tue 2/15/22																				
49	Bathroom Fixtures & Accessories	1 day	Wed 2/16/22	Wed 2/16/22																				
50	Closet Shelving	2 days	Wed 2/16/22	Thu 2/17/22																				
51	Appliances Installation	1 day	Thu 2/17/22	Thu 2/17/22																				
52	Exterior Landscaping	6 days	Fri 2/18/22	Mon 2/28/22																				
53	Substantial Completion	22 days	Tue 3/1/22	Wed 3/30/22																				
54	Snagging	22 days	Tue 3/1/22	Wed 3/30/22																				
55	Snagging	22 days	Tue 3/1/22	Wed 3/30/22																				

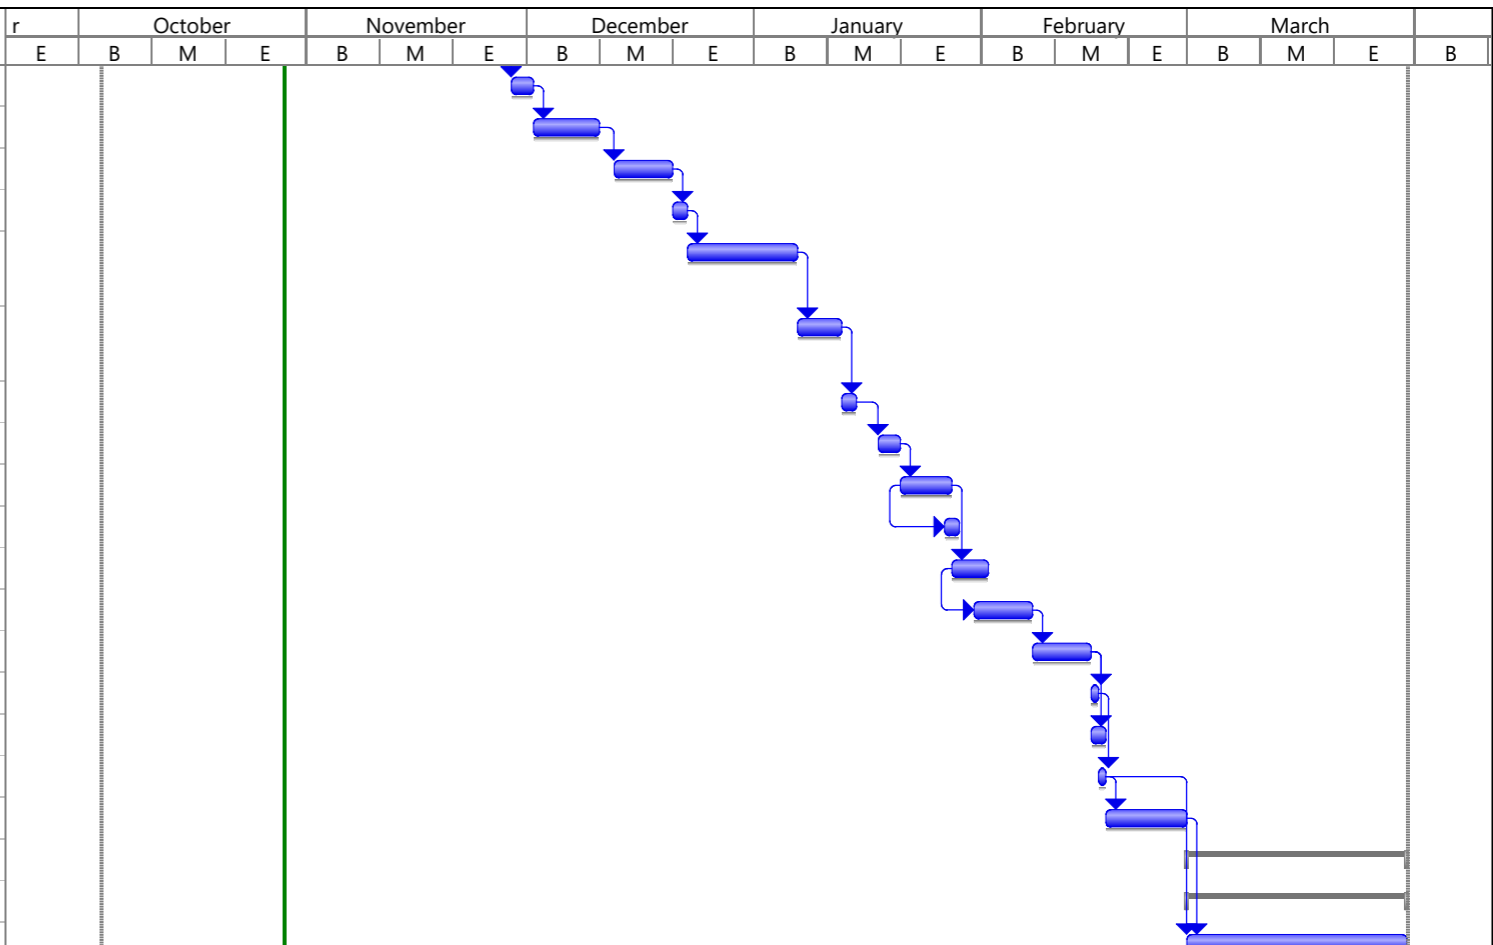

Project: 20 Colonial Drive, New Date: Fri 10/29/21	Task		Milestone		Project Summary		External Milestone		Progress	
	Split		Summary		External Tasks		Deadline			


ID	Task Name	Duration	Start	Finish	March		May		July		September		November		January		March		May				
					E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	
1	Coweta County Fire Station # 9	314 days	Thu 4/14/22	Tue 7/11/23																			
2	Phase 1 Request for Qualification	64 days	Thu 4/14/22	Thu 7/14/22																			
3	Industry Conference	3 days	Thu 4/14/22	Mon 4/18/22																			
4	Issuance of RFQ	1 day	Mon 5/16/22	Mon 5/16/22																			
5	Qualifications receiving	1 day	Mon 5/16/22	Mon 5/16/22																			
6	Complete evaluation/ Selection	20 days	Thu 6/16/22	Thu 7/14/22																			
7	Phase 2 Request for Proposal	75 days	Thu 6/16/22	Fri 9/30/22																			
8	Pre Proposal conf./ Draft RFP review	10 days	Thu 6/16/22	Wed 6/29/22																			
9	Issuance of RFP	1 day	Mon 7/18/22	Mon 7/18/22																			
10	Proposal acceptance/ review	15 days	Tue 8/16/22	Tue 9/6/22																			
11	Anticipated contract award	1 day	Fri 9/16/22	Fri 9/16/22																			
12	Selection Decision	1 day	Fri 9/30/22	Fri 9/30/22																			
13	Construction	185 days	Mon 10/10/22	Mon 7/3/23																			
14	Land Development	50 days	Mon 10/10/22	Tue 12/20/22																			
15	Pre Construction Meeting	2 days	Mon 10/10/22	Tue 10/11/22																			
16	Installation of Erosion Control Measures	5 days	Tue 10/11/22	Mon 10/17/22																			
17	Cleaning & Grinding	5 days	Tue 10/18/22	Mon 10/24/22																			
18	Chip Removal	4 days	Tue 10/25/22	Fri 10/28/22																			
19	Slope Stakes	2 days	Mon 10/31/22	Tue 11/1/22																			
20	BMP Pond Construction	4 days	Wed 11/2/22	Mon 11/7/22																			
21	Mass Grading	2 days	Tue 11/8/22	Wed 11/9/22																			
22	Rough Lot Grading	3 days	Thu 11/3/22	Mon 11/7/22																			
23	Stake Sanitary Sewer	1 day	Thu 11/10/22	Thu 11/10/22																			
24	Sanitary Sewer	2 days	Mon 11/14/22	Tue 11/15/22																			
25	Stake Storm Sewer	1 day	Wed 11/16/22	Wed 11/16/22																			
26	Storm Sewer	3 days	Thu 11/17/22	Mon 11/21/22																			
27	Build Inverts	3 days	Tue 11/22/22	Fri 11/25/22																			
28	Stake Curb	1 day	Mon 11/28/22	Mon 11/28/22																			
29	Curb	3 days	Tue 11/29/22	Thu 12/1/22																			
30	Throats & Tops	3 days	Fri 12/2/22	Tue 12/6/22																			
31	Stake Waterline	1 day	Fri 12/2/22	Fri 12/2/22																			
32	Water Line	3 days	Mon 12/5/22	Wed 12/7/22																			
33	Finish Lot Grading	2 days	Thu 12/8/22	Fri 12/9/22																			
34	Dry Utility Crossing	2 days	Mon 12/12/22	Tue 12/13/22																			
35	Sub grade Prep	1 day	Wed 12/14/22	Wed 12/14/22																			
36	Adjust Manholes	2 days	Thu 12/15/22	Fri 12/16/22																			
37	Paving	2 days	Mon 12/19/22	Tue 12/20/22																			
38	Sub Structure	39 days	Wed 12/21/22	Thu 2/16/23																			
39	Site Preparations	3 days	Wed 12/21/22	Fri 12/23/22																			
40	Leveling & Compaction Under Footings W/ Test	2 days	Tue 12/27/22	Wed 12/28/22																			
41	Anti Termite & Polythene Sheet	1 day	Thu 12/29/22	Thu 12/29/22																			
42	Layout for Column footings & strip footings	1 day	Thu 12/29/22	Thu 12/29/22																			
43	Steel Reinforcement for Reinf Column's Footings & Strip Footings	4 days	Fri 12/30/22	Thu 1/5/23																			

Project: Coweta County Fire Sta; Date: Sun 4/17/22

Task Milestone Project Summary External Milestone Progress

Split Summary External Tasks Deadline


ID	Task Name	Duration	Start	Finish	March		May		July			September			November			January			March			May		
					E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E
44	Form Work of Strip Footing and column footings	2 days	Thu 1/5/23	Fri 1/6/23																						
45	Steel Dowels placement for Stem Wall and Columns Pedestals	1 day	Mon 1/9/23	Mon 1/9/23																						
46	Casting of Footings	1 day	Tue 1/10/23	Tue 1/10/23																						
47	Stripping Formwork & Curing	1 day	Thu 1/12/23	Thu 1/12/23																						
48	Waterproofing of Footing	1 day	Fri 1/13/23	Fri 1/13/23																						
49	Steel Reinforcement for Reinforced Piers Up to slab on grade.	2 days	Tue 1/17/23	Wed 1/18/23																						
50	Side Formwork for Piers	1 day	Thu 1/19/23	Thu 1/19/23																						
51	Casting of Piers	1 day	Fri 1/20/23	Fri 1/20/23																						
52	Stripping Formwork & Curing	1 day	Tue 1/24/23	Tue 1/24/23																						
53	Masonry Stem Walls Construction	3 days	Wed 1/25/23	Fri 1/27/23																						
54	Backfilling Up to Bottom Slab	3 days	Thu 1/26/23	Mon 1/30/23																						
55	Under slab sand blinding & damp proof membrane	2 days	Tue 1/31/23	Wed 2/1/23																						
56	Reinforcement of slab on grade	4 days	Wed 2/1/23	Mon 2/6/23																						
57	Underground MEP Works	5 days	Tue 2/7/23	Mon 2/13/23																						
58	Concrete Pouring of slab on grade	1 day	Tue 2/14/23	Tue 2/14/23																						
59	Curing	1 day	Thu 2/16/23	Thu 2/16/23																						
60	Super Structure	21 days	Fri 2/17/23	Fri 3/17/23																						
61	Structural Works	21 days	Fri 2/17/23	Fri 3/17/23																						
62	Strip templates / Layout walls & Col.	1 day	Fri 2/17/23	Fri 2/17/23																						
63	Steel Columns Erection	4 days	Mon 2/20/23	Thu 2/23/23																						
64	Masonry Wall Construction	4 days	Fri 2/24/23	Wed 3/1/23																						
65	Load Bearing Stud Walls	2 days	Tue 2/28/23	Wed 3/1/23																						
66	Steel Beam Placement at Mezzanine Level	1 day	Thu 3/2/23	Thu 3/2/23																						
67	Channel Framing at Mezzanine Level	1 day	Fri 3/3/23	Fri 3/3/23																						
68	Plywood Deck Placement at Mezzanine Level	1 day	Mon 3/6/23	Mon 3/6/23																						
69	Steel Girders, Beams & Purlins Placement at Roof Level	6 days	Tue 3/7/23	Tue 3/14/23																						
70	Metal Roof Deck Placement at Roof Level	2 days	Wed 3/15/23	Thu 3/16/23																						
71	Inspection of Structure	1 day	Fri 3/17/23	Fri 3/17/23																						
72	Non Load Bearing Wall	25 days	Mon 3/20/23	Fri 4/21/23																						
73	Interior Dry Walls Studs- Ground Floor	3 days	Mon 3/20/23	Wed 3/22/23																						
74	Interior Dry Walls Studs- Mezzanine	1 day	Thu 3/23/23	Thu 3/23/23																						
75	Dry Walls Inspection Before Gypsum Board Installation	5 days	Wed 4/12/23	Tue 4/18/23																						
76	Insulation In Walls - Ground Floor	1 day	Wed 4/19/23	Wed 4/19/23																						
77	Insulation In Walls - First Floor	1 day	Thu 4/20/23	Thu 4/20/23																						
78	Dry Wall Gypsum Board & Sheathing- Ground Floor	2 days	Thu 4/20/23	Fri 4/21/23																						
79	Dry Wall Gypsum Board & Sheathing- First Floor	1 day	Fri 4/21/23	Fri 4/21/23																						
80	MEP Rough-In	14 days	Thu 3/23/23	Tue 4/11/23																						
81	Waste & Vent- Ground Floor	5 days	Thu 3/23/23	Wed 3/29/23																						
82	Waste & Vent- Mezzanine	1 day	Wed 3/29/23	Wed 3/29/23																						
83	Water Supply- Ground Floor	5 days	Thu 3/23/23	Wed 3/29/23																						
84	Water Supply- Mezzanine	1 day	Wed 3/29/23	Wed 3/29/23																						

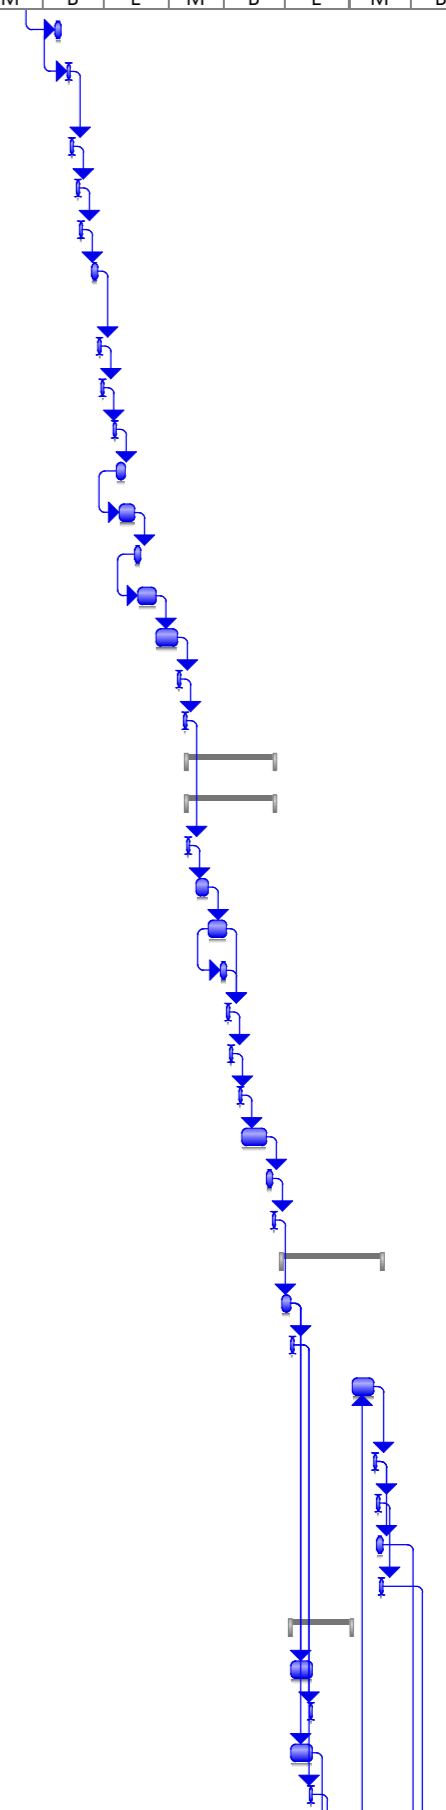

Project: Coweta County Fire Sta; Date: Sun 4/17/22

Task Milestone Project Summary External Milestone Progress
 Split Summary External Tasks Deadline

ID	Task Name	Duration	Start	Finish	March		May			July			September			November			January			March			May		
					E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M
85	Rough Mech. & Fire Safety- Ground Floor	4 days	Thu 3/30/23	Tue 4/4/23																							
86	Rough Mech. & Fire Safety- Mezzanine	1 day	Tue 4/4/23	Tue 4/4/23																							
87	Rough Electrical boxing- Ground Floor	3 days	Wed 4/5/23	Fri 4/7/23																							
88	Rough Electrical boxing- Mezzanine	1 day	Fri 4/7/23	Fri 4/7/23																							
89	Rough Electrical wiring- Ground Floor	3 days	Fri 4/7/23	Tue 4/11/23																							
90	Rough Electrical wiring- Mezzanine	1 day	Tue 4/11/23	Tue 4/11/23																							
91	Finishes	60 days	Mon 4/10/23	Mon 7/3/23																							
92	Scaffold up	7 days	Mon 4/10/23	Tue 4/18/23																							
93	Standing seam metal roofing	7 days	Fri 4/14/23	Mon 4/24/23																							
94	Placement of Exterior Finishes & Materials	20 days	Tue 4/25/23	Mon 5/22/23																							
95	Windows Installation	4 days	Tue 5/23/23	Fri 5/26/23																							
96	Clean windows	2 days	Fri 5/26/23	Tue 5/30/23																							
97	Scaffold down	3 days	Wed 5/31/23	Fri 6/2/23																							
98	Interior Paint Beams & Slab - Roof Level	5 days	Tue 4/25/23	Mon 5/1/23																							
99	Interior Paint Beams & Slab - Mezzanine	1 day	Tue 5/2/23	Tue 5/2/23																							
100	ACT Ceiling Framing & Gypsum Board- Ground Floor	4 days	Tue 5/2/23	Fri 5/5/23																							
101	Ceiling Framing & Gypsum Board- Mezzanine	1 day	Fri 5/5/23	Fri 5/5/23																							
102	Doors & Trim - Ground Floor	6 days	Mon 5/8/23	Mon 5/15/23																							
103	Doors & Trim- Mezzanine	1 day	Tue 5/16/23	Tue 5/16/23																							
104	Interior Paint Walls & Columns - Ground Floor	8 days	Tue 5/16/23	Thu 5/25/23																							
105	Interior Paint Walls & Columns- Mezzanine	2 days	Thu 5/25/23	Fri 5/26/23																							
106	Paint Doors & Trim - Level 1	4 days	Wed 5/24/23	Tue 5/30/23																							
107	Paint Doors & Trim - Level 2	1 day	Wed 5/31/23	Wed 5/31/23																							
108	Cabinets - Ground Floor	4 days	Fri 5/26/23	Thu 6/1/23																							
109	Countertops - Ground Floor	1 day	Fri 6/2/23	Fri 6/2/23																							
110	Tile Backsplashes - Ground Floor	1 day	Mon 6/5/23	Mon 6/5/23																							
111	Rest Room Wall Porcelain Tiles- Ground Floor	7 days	Mon 6/5/23	Tue 6/13/23																							
112	Flooring- Ground Floor	5 days	Wed 6/14/23	Tue 6/20/23																							
113	Flooring- First Floor	1 day	Wed 6/21/23	Wed 6/21/23																							
114	Finish Hardware - Ground Floor	1 day	Wed 6/21/23	Wed 6/21/23																							
115	Finish Hardware - Mezzanine	1 day	Wed 6/21/23	Wed 6/21/23																							
116	Finish MEP - Ground Floor	4 days	Thu 6/22/23	Tue 6/27/23																							
117	Finish MEP - First Floor	1 day	Wed 6/28/23	Wed 6/28/23																							
118	Bath & Kitchen Fixtures & Accs. - Ground Floor	2 days	Wed 6/28/23	Thu 6/29/23																							
119	Closet Shelving - Ground Floor	1 day	Fri 6/30/23	Fri 6/30/23																							
120	Appliances- Ground Floor	1 day	Mon 7/3/23	Mon 7/3/23																							
121	Substantial Completion	5 days	Wed 7/5/23	Tue 7/11/23																							
122	Inspections	5 days	Wed 7/5/23	Tue 7/11/23																							
123	Punch Listing	5 days	Wed 7/5/23	Tue 7/11/23																							

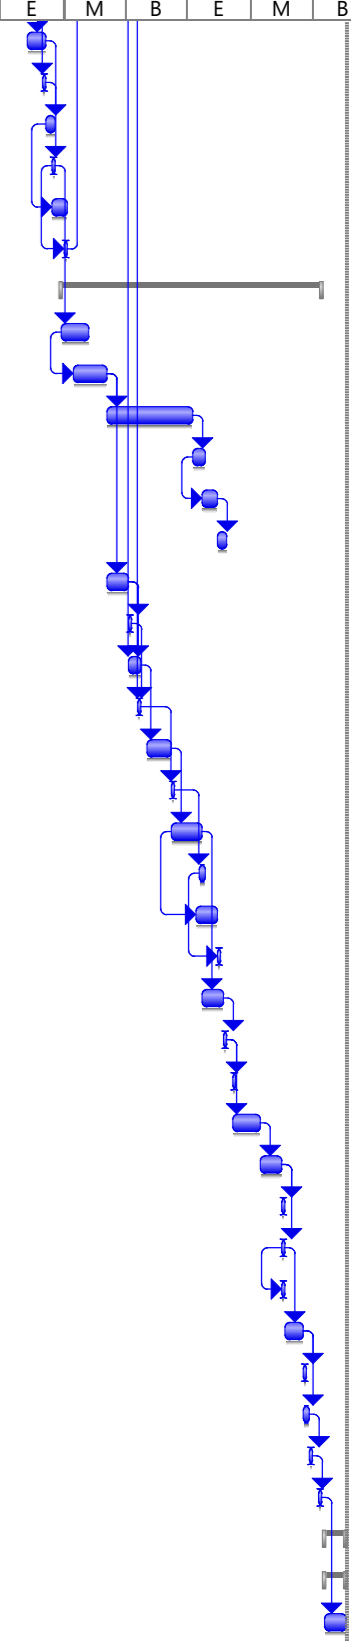


Project: Coweta County Fire Sta
Date: Sun 4/17/22

Task Milestone Project Summary External Milestone

Split Summary External Tasks Deadline


Progress

ID	Task Name	Duration	Start	Finish	January 1			January 21			February 11			March 1		March 21		
					1/2	1/9	1/16	1/23	1/30	2/6	2/13	2/20	2/27	3/6	3/13	3/20	3/27	
1	Four Bedroom Apartment	59 days	Wed 1/5/22	Wed 3/30/22														
2	Notice to Proceed	1 day	Wed 1/5/22	Wed 1/5/22														
3	Notice to Proceed	0 days	Wed 1/5/22	Wed 1/5/22														
4	Mobilization	1 day	Wed 1/5/22	Wed 1/5/22														
5	Non Load Bearing Wall	19 days	Thu 1/6/22	Wed 2/2/22														
6	Gypsum Board Placement at One Side of Existing Framing	1 day	Thu 1/6/22	Thu 1/6/22														
7	MEP Rough Ins In Internal Stud Walls	5 days	Fri 1/7/22	Thu 1/13/22														
8	Dry Walls Inspection Before Gypsum Board Installation	2 days	Fri 1/28/22	Mon 1/31/22														
9	Insulation In Walls	1 day	Tue 2/1/22	Tue 2/1/22														
10	Gypsum Board Placement at Other Side of Stud Wall & Sheathing	1 day	Wed 2/2/22	Wed 2/2/22														
11	MEP Rough-In	14 days	Fri 1/7/22	Thu 1/27/22														
12	Waste & Vent	4 days	Fri 1/7/22	Wed 1/12/22														
13	Water Supply	4 days	Fri 1/7/22	Wed 1/12/22														
14	Rough Fire Fighting System	3 days	Thu 1/13/22	Tue 1/18/22														
15	Rough Electrical boxing	4 days	Wed 1/19/22	Mon 1/24/22														
16	Rough Electrical wiring	3 days	Tue 1/25/22	Thu 1/27/22														
17	Finishes	50 days	Fri 1/14/22	Fri 3/25/22														
18	Cladding Works	20 days	Fri 1/14/22	Fri 2/11/22														
19	Scaffold up	6 days	Fri 1/14/22	Mon 1/24/22														
20	Roofing Finishes	5 days	Fri 1/21/22	Thu 1/27/22														
21	Placement of Exterior Finishes & Materials	8 days	Fri 1/28/22	Tue 2/8/22														
22	Scaffold down	3 days	Wed 2/9/22	Fri 2/11/22														
23	Ceiling Works	4 days	Thu 2/3/22	Tue 2/8/22														
24	Ceiling Framing	2 days	Thu 2/3/22	Fri 2/4/22														
25	Ceiling Insulation	1 day	Mon 2/7/22	Mon 2/7/22														
26	Gypsum Board Placement	1 day	Tue 2/8/22	Tue 2/8/22														
27	Wall & Ceiling Finishes	6 days	Wed 2/9/22	Wed 2/16/22														
28	Internal Paint Works (Primer - Initial Coat)	4 days	Wed 2/9/22	Mon 2/14/22														
29	Internal Paint Works (Final Coat)	3 days	Mon 2/14/22	Wed 2/16/22														
30	Wall Tiling Works	3 days	Mon 2/14/22	Wed 2/16/22														
31	Floor Finishes	4 days	Thu 2/17/22	Tue 2/22/22														
32	Flooring	4 days	Thu 2/17/22	Tue 2/22/22														
33	Doors & Windows	5 days	Wed 2/23/22	Tue 3/1/22														
34	Installation of Doors & Windows/ Clear Panels	3 days	Wed 2/23/22	Fri 2/25/22														
35	Doors & Windows Trims	1 day	Mon 2/28/22	Mon 2/28/22														
36	Paint Doors & Trim	1 day	Tue 3/1/22	Tue 3/1/22														
37	Specialities & Furnishings	18 days	Wed 3/2/22	Fri 3/25/22														
38	Cabinets	5 days	Wed 3/2/22	Tue 3/8/22														
39	Countertops	1 day	Tue 3/8/22	Tue 3/8/22														
40	Tile Backsplashes	2 days	Wed 3/9/22	Thu 3/10/22														
41	Finish Hardware	1 day	Wed 3/9/22	Wed 3/9/22														

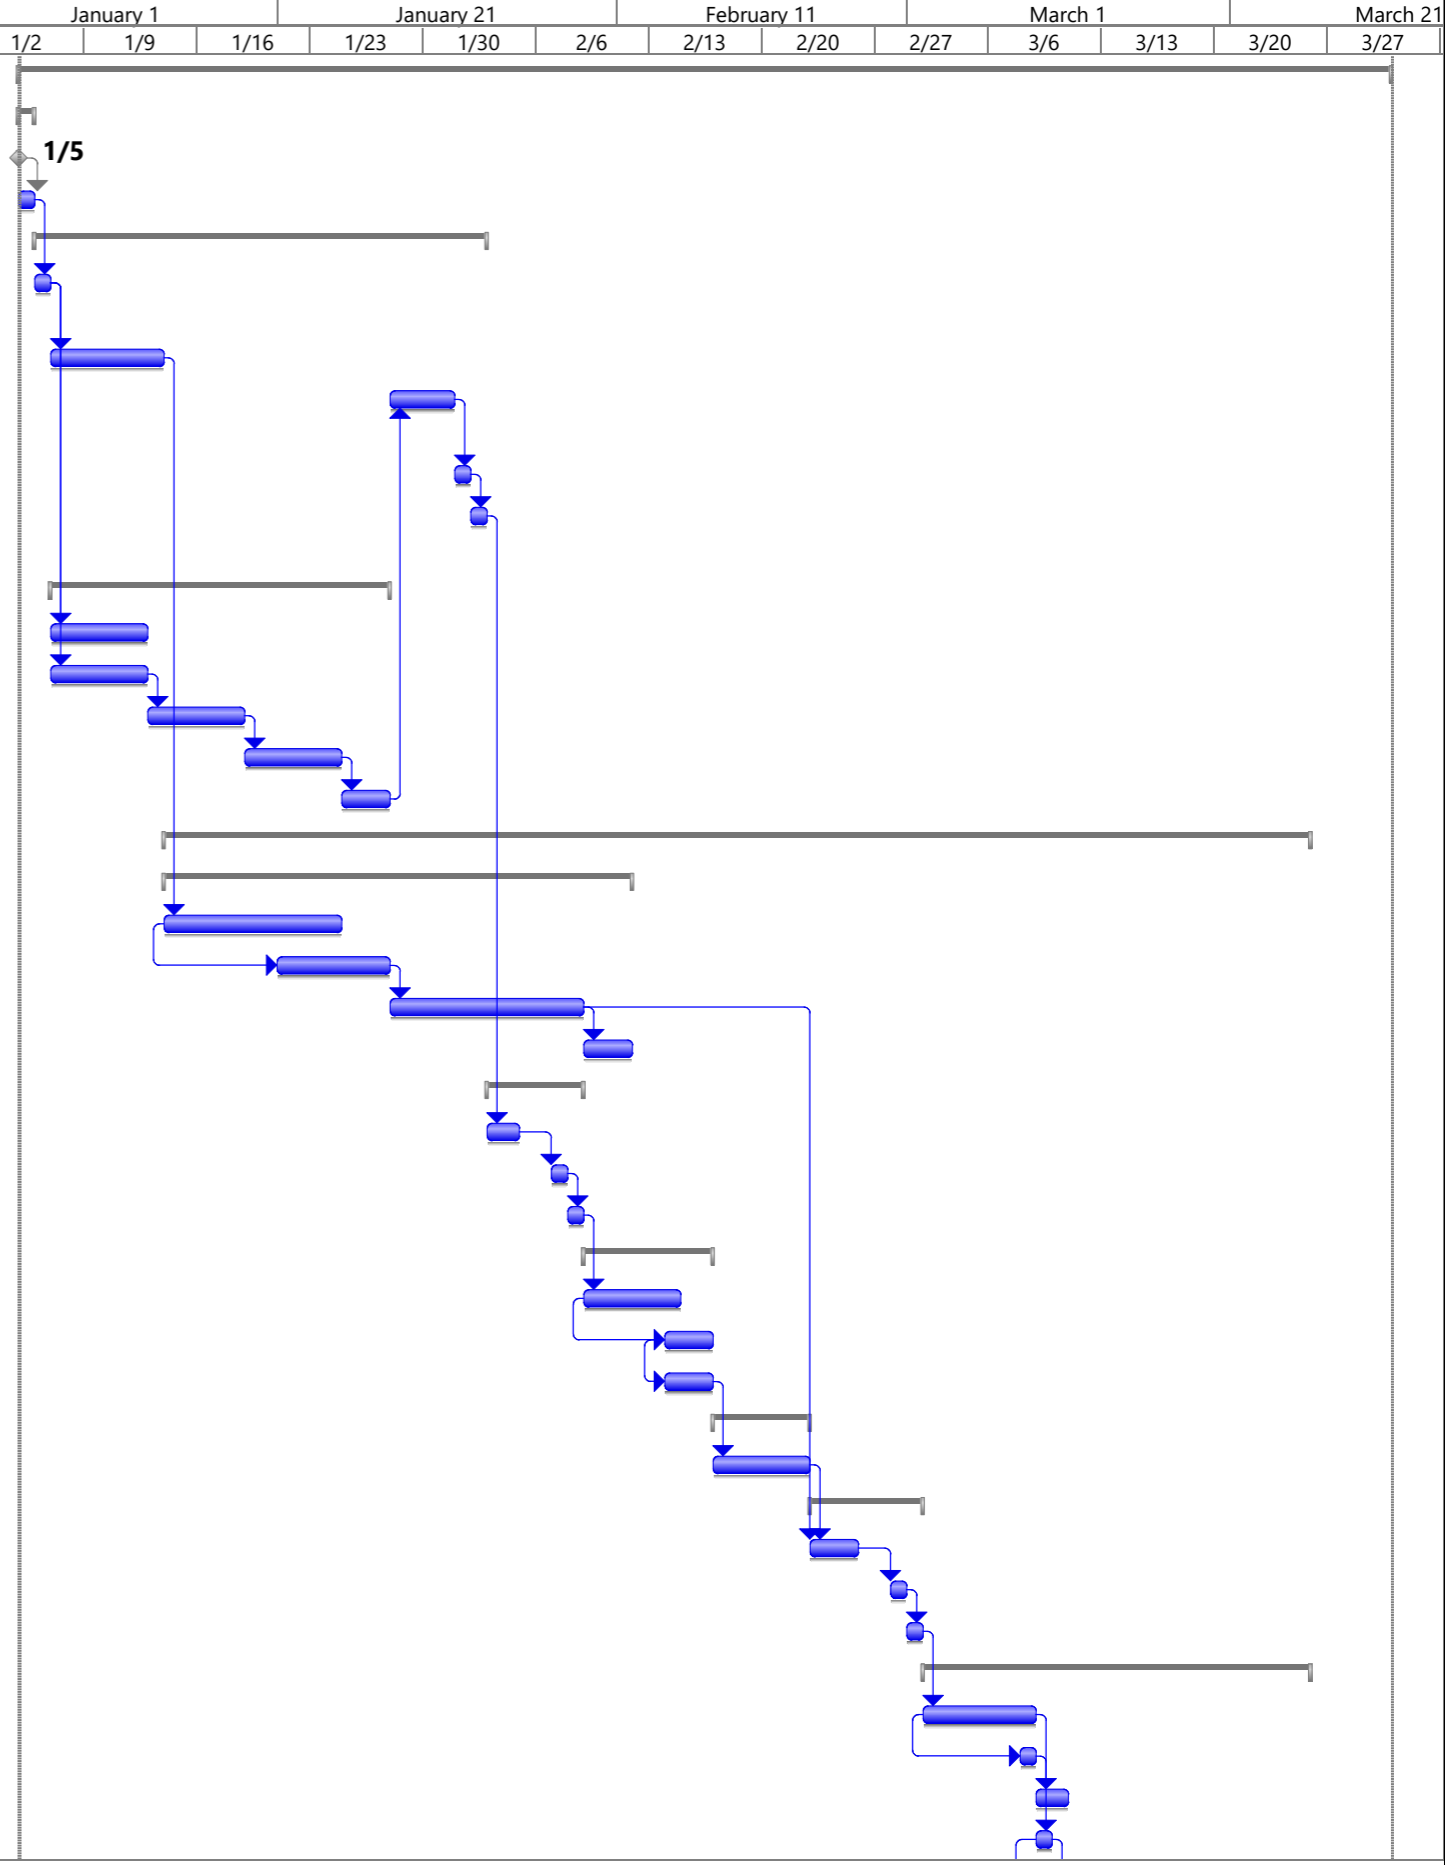

Project: 4 Bedroom Apartment Date: Mon 12/6/21	Task	Milestone	Project Summary	External Milestone	Progress
	Split	Summary	External Tasks	Deadline	

ID	Task Name	Duration	Start	Finish	January 1			January 21			February 11			March 1			March 21	
					1/2	1/9	1/16	1/23	1/30	2/6	2/13	2/20	2/27	3/6	3/13	3/20	3/27	
42	Finish MEP	6 days	Thu 3/10/22	Thu 3/17/22														
43	Bath & Kitchen Fixtures & Accs.	2 days	Fri 3/18/22	Mon 3/21/22														
44	Closet Shelving	2 days	Wed 3/9/22	Thu 3/10/22														
45	Appliances	1 day	Tue 3/22/22	Tue 3/22/22														
46	Furniture & decorative accessories for bedrooms	3 days	Wed 3/23/22	Fri 3/25/22														
47	Substantial Completion	2 days	Mon 3/28/22	Wed 3/30/22														
48	Inspections	2 days	Mon 3/28/22	Wed 3/30/22														
49	Punch Listing	2 days	Mon 3/28/22	Wed 3/30/22														

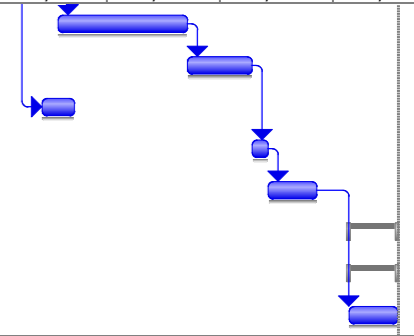

Project: 4 Bedroom Apartment Date: Mon 12/6/21	Task		Milestone		Project Summary		External Milestone		Progress	
	Split		Summary		External Tasks		Deadline			
